


EQ-01 SF-S06 / SF-S08 bearings over the FF windows FF-WF02 / FF-WF19 (S-102, S-121)

Status: Open | see GS-02

ICF model (GS-02)

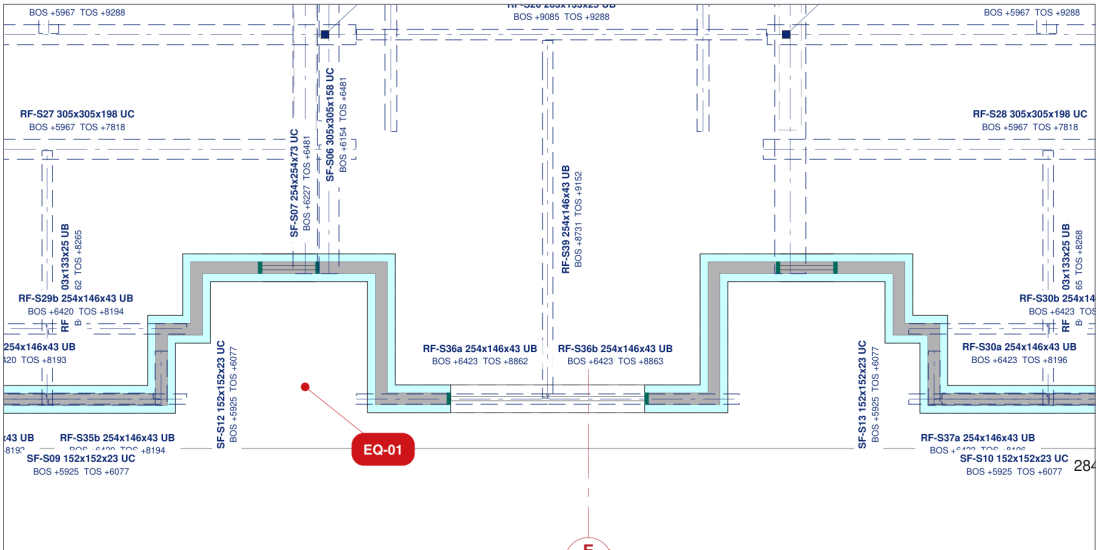

ISSUE The second-floor transfer beams SF-S06 (UC 305x305x158, x 6370) and SF-S08 (UC 356x406x287, x 12586) bear on the south wall (L2, top 174.975 AOD) directly over the 685-wide FF windows either side of the entrance bay. At TOS 175.229 the beam undersides are 6252 (S06) and 6185 (S08) above the slab datum; the architect's window head is 6023, leaving 229 mm (S06) and 162 mm (S08) of wall between head and beam. S-121 schedules an RCB152 x 300 - 2H16 lintel there, which would reach 6323, 71 mm into SF-S06 and 138 mm into SF-S08.

QUESTION Please confirm the bearing detail: a steel spreader under each beam end (model assumption UC 152x152x30, 1285 long, 300 bearing each side, TOS = beam underside), or a revised lintel / beam arrangement. The window positions are the architect's and are held.

ENGINEER'S RESPONSE

Name / date:

QUESTIONS REGISTER

QUERIES

Ref	Subject	Drawing	Status
EQ-01	SF-S06 / SF-S08 bearings over the FF windows FF-WF02 / FF-WF19 (S-102, S-121)	GS-02	Open

NOTES

- Questions raised on the ICF approval drawings against the structural engineer's drawing Tier Consult 078-TCE-DEN-XX-DR-S-096..210 rev -.
- Each panel shows the engineer's drawing beside the architect's drawing and/or the ICF model, cropped to the same area.
- Please answer in the response box of each question (or by email quoting the EQ reference); the approval drawings will be revised to suit.
- EQ tags on the GA drawings link to these panels.

REVISIONS

REV	DATE	DESCRIPTION
P01	23.09.26	Approval issue



CLIENT

ICF Homes

PROJECT

Dendrons

DRAWING TITLE

QUESTIONS FOR THE ENGINEER

Structural queries on the ICF approval drawings - sheet 1 of 1

SCALE	SIZE	DATE	DRAWN
NTS	A3	23.09.26	TS
STATUS		DRAWING No.	
FOR APPROVAL		UKPCS-003-EQ-01	
		REV	
		P01	
